


ID	Task Name	Duration	Start	Finish	2009				2010				2011				20			
					tr	tr	tr	tr	tr	tr	tr	tr	tr	tr	tr	tr	tr			
1	<b>Project Planning and Procurement</b>	<b>75 days</b>	<b>Wed 3/11/09</b>	<b>Tue 6/23/09</b>																
2	DOE to complete modification of existing IAG to add reporting requirements and fu	0 days	Wed 3/11/09	Wed 3/11/09																
3	EPA begin review of modified IAG	5 days	Wed 3/11/09	Tue 3/17/09																
4	EPA complete review of IAG	0 days	Tue 3/17/09	Tue 3/17/09																
5	DOE negotiate and revise IAG	5 days	Wed 3/18/09	Tue 3/24/09																
6	Award modification	0 days	Tue 3/24/09	Tue 3/24/09																
7	EPA to complete project planning and staffing	22 days	Wed 3/25/09	Thu 4/23/09																
8	EPA Provide DOE with their detailed approach to reporting	0 days	Thu 4/23/09	Thu 4/23/09																
9	DOE Review and comment on reporting	5 days	Fri 4/24/09	Thu 4/30/09																
10	EPA revision of reporting approach	5 days	Fri 5/1/09	Thu 5/7/09																
11	DOE approval of reporting approach	0 days	Thu 5/7/09	Thu 5/7/09																
12	EPA to finalize procurement strategy	10 days	Wed 4/15/09	Tue 4/28/09																
13	Procurement of contractor	25 days	Wed 4/29/09	Tue 6/2/09																
14	EPA to complete contractor procurement	15 days	Wed 6/3/09	Tue 6/23/09																
15	<b>Gamma Scanning</b>	<b>345 days</b>	<b>Wed 6/24/09</b>	<b>Tue 10/19/10</b>																
16	EPA to procure materials and construct gamma scanning device	6 mons	Wed 6/24/09	Tue 12/8/09																
17	EPA to complete draft gamma scan survey work plan	20 days	Wed 6/24/09	Tue 7/21/09																
18	Contractor to complete HASP	20 days	Wed 6/24/09	Tue 7/21/09																
19	Stakeholder review of gamma scan survey work plan	15 days	Wed 7/22/09	Tue 8/11/09																
20	Revision of gamma scan survey work plan	10 days	Wed 8/12/09	Tue 8/25/09																
21	EPA finalization of gamma scan survey work plan	0 days	Tue 8/25/09	Tue 8/25/09																
22	Conduct Phase I gamma scanning survey	4 mons	Wed 8/26/09	Tue 12/15/09																
23	Conduct Phase II gamma scanning survey	7 mons	Wed 4/7/10	Tue 10/19/10																
24	Complete gamma scan survey	0 days	Tue 10/19/10	Tue 10/19/10																
25	Complete background study	0 days	Mon 5/3/10	Mon 5/3/10																
26	<b>Complete Historical Site Assessment</b>	<b>240 days</b>	<b>Wed 6/24/09</b>	<b>Tue 5/25/10</b>																
27	Start Area IV/Buffer Zone Historical Site Assessment activities	12 mons	Wed 6/24/09	Tue 5/25/10																
28	Complete Area IV/Buffer Zone Historical Site Assessment Report	0 days	Tue 5/25/10	Tue 5/25/10																
29	<b>Complete Scoping/Characterization Surveys</b>	<b>410 days</b>	<b>Mon 2/22/10</b>	<b>Fri 9/16/11</b>																
30	<b>Prepare Area IV/Buffer Zone Work Plan (FSP/QAPP)</b>	<b>140 days</b>	<b>Mon 2/22/10</b>	<b>Fri 9/3/10</b>																
31	EPA to prepare draft work plan	90 days	Mon 2/22/10	Fri 6/25/10																

Project: SSFL_OnsiteSchedule Date: Mon 3/16/09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	

ID	Task Name	Duration	Start	Finish	2009				2010				2011				20		
					tr	tr	tr	tr	tr	tr	tr	tr	tr	tr	tr	tr	tr		
32	Stakeholder review	30 days	Mon 6/28/10	Fri 8/6/10															
33	Revise work plan	20 days	Mon 8/9/10	Fri 9/3/10															
34	Work plan completed	0 days	Fri 9/3/10	Fri 9/3/10															
35	<b>Area IV/Buffer Area Field Work</b>	<b>200 days</b>	<b>Mon 9/6/10</b>	<b>Fri 6/10/11</b>															
36	Perform 1st third of surface/subsurface sampling at Area IV	3 mons	Mon 9/6/10	Fri 11/26/10															
37	Perform 1st third of surface/subsurface sampling at buffer zone	3 mons	Mon 9/6/10	Fri 11/26/10															
38	Perform 2nd third of surface/subsurface sampling at Area IV	3 mons	Mon 11/29/10	Fri 2/18/11															
39	Perform 2nd third of surface/subsurface sampling at buffer zone	3 mons	Mon 11/29/10	Fri 2/18/11															
40	Perform Phase I groundwater/surface water sampling	2 mons	Mon 11/29/10	Fri 1/21/11															
41	Perform 3rd third of surface/subsurface sampling at Area IV	3 mons	Mon 2/21/11	Fri 5/13/11															
42	Perform 3rd third of surface/subsurface sampling at buffer zone	3 mons	Mon 2/21/11	Fri 5/13/11															
43	Perform Phase I groundwater/surface water sampling	2 mons	Mon 3/21/11	Fri 5/13/11															
44	Validate Data	9 mons	Mon 10/4/10	Fri 6/10/11															
45	Complete Area IV/buffer zone rad. char. survey	0 days	Fri 6/10/11	Fri 6/10/11															
46	<b>Complete Report</b>	<b>210 days</b>	<b>Mon 11/29/10</b>	<b>Fri 9/16/11</b>															
47	EPA to complete data evaluation and draft report	8.5 mons	Mon 11/29/10	Fri 7/22/11															
48	Stakeholder review of draft report	1 mon	Mon 7/25/11	Fri 8/19/11															
49	Report Revision	1 mon	Mon 8/22/11	Fri 9/16/11															
50	Complete Area IV/Buffer Zone Data Evaluation & Report	0 days	Fri 9/16/11	Fri 9/16/11															

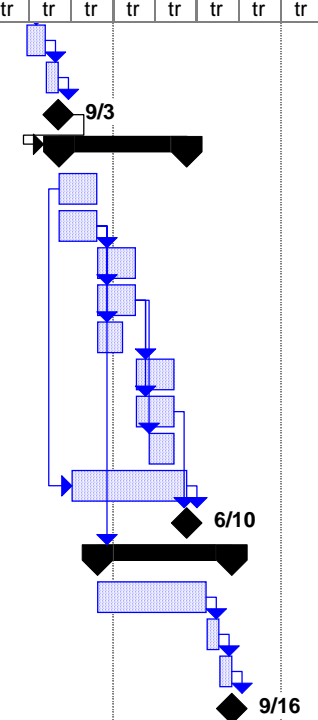

Project: SSFL_OnsiteSchedule Date: Mon 3/16/09	Task		Milestone		External Tasks	
	Split		Summary		External Milestone	
	Progress		Project Summary		Deadline	
